


Gas Tightness Test									
Gas tightness test carried out (Yes / No)	Yes	Total Installation volume (m ³)	0.001056	Max allowable pressure drop (mbar)	4	Type of gauge used (water / electronic)	Electric	Tightness test result (Pass / Fail)	
Where was the Test carried out from?	ECV	Let by test duration (mins)	1	Volume smallest occupied space (m ³)		Smell of gas	No	Pass	
Scope of work (e.g. IGE/UP/1 or 1A or 1B)	IGE/UP/1B	Stabilisation period (mins)	1	Tightness test pressure (TTP) (mbar)	20	CO Alarm			
						CO Alarm Installed	Date Of Expiry	CO Pass/Fail	
Installation (New / Existing / Extension)	Existing	Tightness test duration (mins)	2	Actual pressure drop (mbar)	0.5	Yes	21/09/21 date of manufacture (10 yrs)	Pass	
Meter Information									
Meter Location	Externally front of property	Meter room secure	Meter box	Meter room key labelled	Meter box key	Standing pressure at meter (mbar)	23.19	Working pressure at Appliances (mbar)	
Meter size	U6	Meter accessible	Yes	Meter room ventilated	N/a	Working pressure at meter	21	20.83	
ECV labelled	Yes	Does ECV operate easily	Yes	Adequate gas isolation	Yes	Suitably sleeved Area Adjacent Meter	Yes	Meter Labelling Correct	
Pipework colour coded /identified from point of Test	Yes	Line diagram at meter (current)	N/a	Clear of combustibles	Yes	Installation cross bonded	Yes internally	Yes	
Gas pipe supported (Where Visible) from point of Test	Yes				Flue Dilution (CO ₂) %	N/a	Air Sample (CO ₂) %	N/a	
Manometer Make	Testo	Serial No	N/a	Analyser Make	Testo	Serial No	61857248		
Description of work: Tightness test, boiler service and co alarm tested									
Defects				Remedial work required					
No 1	Boiler cover hinges broken			Replace cover and hinges					
No 2	Flue air test point disintegrated on removal			Replaced flue air test point cap on service					
No 3									
No 4									
No 5									
No 6									
No 7									
No 8									
Parts used			Part Number		Qty		Declaration of Gas safety: I confirm that all of the work described on this form has been satisfactorily completed in accordance with the current Gas Safety (Installation & Use) regulations, industry standards and procedures.		
Flue air test point cap					1				
Print Name	Sean Moloney		Engineer's Signature						
The work has been carried out to my satisfaction. I agree to pay for all chargeable work carried out and the cost of any parts ordered and/or supplied.									
Print Name	No person present		Customer Signature						

Tightness Test Carried out from this Valve 'Label'



Appliance Flue Termination



Warning Label 'if Applicable'

CO Expiry Date

Location of CO Alarm

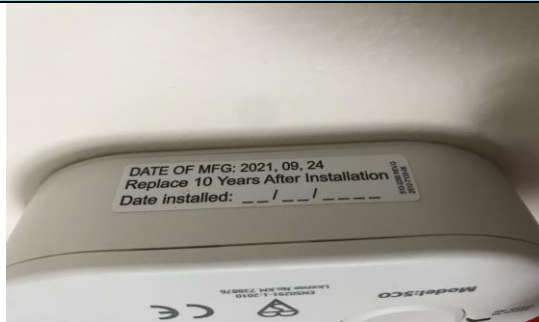




Photo of Unsafe Situation	Defect 1	Defect 2
	 A photograph showing the control panel of a white washing machine. The panel features a circular dial, several buttons, and a prominent warning label with a barcode and text. The label includes the heading "No Hot Water" and other safety instructions.	 A photograph of a white cylindrical object, possibly a fire extinguisher or a sensor, mounted on a wall. It has a red label with a white figure and some text. The object is positioned in a corner of a room.
Defect 3	Defect 4	Defect 5
Defect 6	Defect 7	Defect 8
