


Gas Tightness Test									
Gas tightness test carried out (Yes / No)	Yes	Total Installation volume (m³)	0.00176	Max allowable pressure drop (mbar)	2.4	Type of gauge used (water / electronic)	Electric	Tightness test result (Pass / Fail)	
Where was the Test carried out from?	ECV	Let by test duration (mins)	1	Volume smallest occupied space (m³)	37.5	Smell of gas	N/A	Pass	
Scope of work (e.g. IGE/UP/1 or 1A or 1B)	IGE/UP/1B	Stabilisation period (mins)	1	Tightness test pressure (TTP) (mbar)	20	CO Alarm			
						CO Alarm Installed	Date Of Expiry	CO Pass/Fail	
Installation (New / Existing / Extension)	Existing	Tightness test duration (mins)	2	Actual pressure drop (mbar)	0	Yes	07/2032	Pass	
Meter Information									
Meter Location	Plant room	Meter room secure	Yes	Meter room key labelled	Card access	Standing pressure at meter (mbar)	21	Working pressure at Appliances (mbar)	
Meter size	U6	Meter accessible	Yes	Meter room ventilated	Yes	Working pressure at meter	20	20	
ECV labelled	Yes	Does ECV operate easily	Yes	Adequate gas isolation	Yes	Suitably sleeved Area Adjacent Meter	Yes	Meter Labelling Correct	
Pipework colour coded /identified from point of Test	Yes	Line diagram at meter (current)	No	Clear of combustibles	Yes	Installation cross bonded	Yes	Yes	
Gas pipe supported (Where Visible) from point of Test	Yes				Flue Dilution (CO ₂) %	N/a	Air Sample (CO ₂) %	N/a	
Manometer Make	Testo	Serial No	N/a	Analyser Make	Testo	Serial No	61857248		
Description of work: Tightness test, boiler service and co alarm tested									
Defects					Remedial work required				
No 1	Condense pump failed causing a water leak into the boiler that has rusted part of boiler case. Checked integrity of boiler case				Condense pump has been changed for new				
No 2	Flue extensions not clipped				Brackets need to be fitted to each extension piece (walls have asbestos in)				
No 3	Bird cage around flue has started to corrode				A new bird cage needs fitting around flue terminal				
No 4									
No 5									
No 6									
No 7									
No 8									
Parts used			Part Number		Qty		Declaration of Gas safety: I confirm that all of the work described on this form has been satisfactorily completed in accordance with the current Gas Safety (Installation & Use) regulations, industry standards and procedures.		
Print Name	Sean Moloney		Engineer's Signature						
The work has been carried out to my satisfaction. I agree to pay for all chargeable work carried out and the cost of any parts ordered and/or supplied.									
Print Name	No person present		Customer Signature						

Tightness Test Carried out from this Valve 'Label'



Appliance Flue Termination



Warning Label 'if Applicable'

CO Expiry Date

Location of CO Alarm


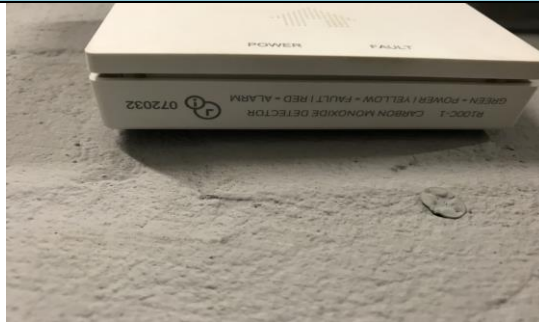


Photo of Unsafe Situation

Defect 1

Defect 2

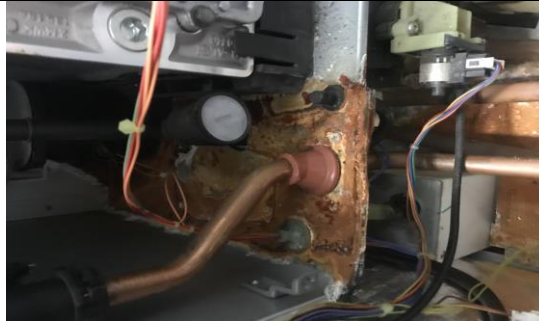

Defect 3

Defect 4

Defect 5



Defect 6

Defect 7

Defect 8
