



**PRT**  
HEATING LTD  
COMMERCIAL | INDUSTRIAL | DOMESTIC

|                                                                                   |  |                       |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
|-----------------------------------------------------------------------------------|--|-----------------------|----------------------------|---------------|------|----------------------------------------------|------|-----|------|-----|------|------|------|-----|------|-----|------|
| Certificate Number                                                                |  | Job Ref               |                            | 21824         |      | Address :<br>Unit 1-2, 403 Broad Lane        |      |     |      |     |      |      |      |     |      |     |      |
| 3679                                                                              |  | Eng. Name             |                            | Jack Williams |      | Coventry<br>CV5 7AX<br>+44 02477170800       |      |     |      |     |      |      |      |     |      |     |      |
|                                                                                   |  | Gas Safe ID No        |                            | 6016603       |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Company Gas safe No : 30909                                                       |  | Work Carried out Date |                            | 01/07/26      |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
|                                                                                   |  | Next Service due Date |                            | 01/07/27      |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Site Address :<br><br>. CC05<br>5 Cryfield Cottage<br>Gibbet Hill Road<br>CV4 7AL |  |                       |                            |               |      | Is the Job Complete                          |      |     |      |     |      | Yes  |      |     |      |     |      |
|                                                                                   |  |                       |                            |               |      | Unsafe situation identified (classification) |      |     |      |     |      | No   |      |     |      |     |      |
| Sheet1 of 3                                                                       |  |                       |                            |               |      | Has a Warning notice been issued             |      |     |      |     |      |      |      |     |      |     |      |
|                                                                                   |  |                       |                            |               |      | Warning notice number                        |      |     |      |     |      |      |      |     |      |     |      |
|                                                                                   |  |                       |                            |               |      | Has the appliance been labelled              |      |     |      |     |      |      |      |     |      |     |      |
| Have you completed all risk assessments : Yes                                     |  |                       |                            |               |      | Has the responsible person been informed     |      |     |      |     |      |      |      |     |      |     |      |
| How many appliances have been tested                                              |  |                       |                            |               |      |                                              |      |     | One  |     |      |      |      |     |      |     |      |
| Appliance No.                                                                     |  |                       | No 1                       |               |      | No 2                                         |      |     | No 3 |     |      | No 4 |      |     |      |     |      |
| Make                                                                              |  |                       | Worcester 30si Compact ERP |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Model                                                                             |  |                       | 30si                       |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Appliance Type                                                                    |  |                       | Condensing Combi boiler    |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Ref No                                                                            |  |                       | N/A                        |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Location                                                                          |  |                       | Kitchen                    |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Condition                                                                         |  |                       | Fair                       |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Appliance No.                                                                     |  |                       | No 5                       |               |      | No 6                                         |      |     | No 7 |     |      | No 8 |      |     |      |     |      |
| Make                                                                              |  |                       |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Model                                                                             |  |                       |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Appliance Type                                                                    |  |                       |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Ref No                                                                            |  |                       |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Location                                                                          |  |                       |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Condition                                                                         |  |                       |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Appliance No                                                                      |  | No1                   |                            | No2           |      | No3                                          |      | No4 |      | No5 |      | No6  |      | No7 |      | No8 |      |
| Flue Type                                                                         |  | Room sealed type C    |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Flue flow satisfactory                                                            |  | N/A                   |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Spillage test satisfactory                                                        |  | N/A                   |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Termination satisfactory                                                          |  | Yes                   |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Visual condition of flue satisfactory                                             |  | Yes                   |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Flame proving satisfactory                                                        |  | Yes                   |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Burner lock out time (seconds)                                                    |  | 2                     |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Temp t/stat operation satisfactory                                                |  | Yes                   |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Ventilation Type                                                                  |  | N/A                   |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Mechanical vent / flue interlock satisfactory                                     |  | N/A                   |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Reqd Ventilation low level (cm²)                                                  |  | N/A                   |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Reqd Ventilation High level (cm²)                                                 |  | N/A                   |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Badged Rating (kW Nett)                                                           |  | 24                    |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Actual Ventilation low level (cm²)                                                |  | N/A                   |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Actual Ventilation High level (cm²)                                               |  | N/A                   |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Ventilation Satisfactory                                                          |  | N/A                   |                            |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Firing Mode                                                                       |  | Low                   | High                       | Low           | High | Low                                          | High | Low | High | Low | High | Low  | High | Low | High | Low | High |
| Heat input rating KW                                                              |  | N/A                   | N/A                        |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Gas Burner Pressure                                                               |  | N/A                   | N/A                        |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Gas Flow Rate m³/hr.                                                              |  | N/A                   | N/A                        |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Ambient (Room) Temperature (°C)                                                   |  | 22.0                  | 21.6                       |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Flue Gas Temperature (°C)                                                         |  | 31.9                  | 47.9                       |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| CO/CO² Ratio                                                                      |  | 0.0000                | 0.0006                     |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Oxygen (O²)%                                                                      |  | 7.4                   | 4.7                        |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Carbon Monoxide (CO) ppm                                                          |  | 3                     | 51                         |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Carbon Dioxide (CO²)%                                                             |  | 7.72                  | 9.22                       |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Excess Air                                                                        |  | 54.2                  | 29.1                       |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |
| Gross Efficiency                                                                  |  | 89.4                  | 88.8                       |               |      |                                              |      |     |      |     |      |      |      |     |      |     |      |

| Gas Tightness Test                                                                                                                                      |                                                                                                  |                                 |                      |                                      |                                                                                     |                                         |                                                                                                                                                                                                                                   |                                       |  |
|---------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------|---------------------------------|----------------------|--------------------------------------|-------------------------------------------------------------------------------------|-----------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------|--|
| Gas tightness test carried out (Yes / No)                                                                                                               | Yes                                                                                              | Total Installation volume (m³)  | 0.0022               | Max allowable pressure drop (mbar)   | 1                                                                                   | Type of gauge used (water / electronic) | Electric                                                                                                                                                                                                                          | Tightness test result (Pass / Fail)   |  |
| Where was the Test carried out from?                                                                                                                    | ECV                                                                                              | Let by test duration (mins)     | 1                    | Volume smallest occupied space (m³)  | N/A                                                                                 | Smell of gas                            | N/A                                                                                                                                                                                                                               | Pass                                  |  |
| Scope of work (e.g. IGE/UP/1 or 1A or 1B)                                                                                                               | IGE/UP/1B                                                                                        | Stabilisation period (mins)     | 1                    | Tightness test pressure (TTP) (mbar) | 20.90                                                                               | CO Alarm                                |                                                                                                                                                                                                                                   |                                       |  |
|                                                                                                                                                         |                                                                                                  |                                 |                      |                                      |                                                                                     | CO Alarm Installed                      | Date Of Expiry                                                                                                                                                                                                                    | CO Pass/Fail                          |  |
| Installation (New / Existing / Extension)                                                                                                               | Existing                                                                                         | Tightness test duration (mins)  | 2                    | Actual pressure drop (mbar)          | 0.05                                                                                | Yes                                     | 10/2035                                                                                                                                                                                                                           | Pass                                  |  |
| Meter Information                                                                                                                                       |                                                                                                  |                                 |                      |                                      |                                                                                     |                                         |                                                                                                                                                                                                                                   |                                       |  |
| Gas Meter Present                                                                                                                                       | Yes                                                                                              | Meter room secure               | N/A                  | Meter room key labelled              | N/A                                                                                 | Standing pressure (mbar)                |                                                                                                                                                                                                                                   | Working pressure at Appliances (mbar) |  |
| Meter size                                                                                                                                              | U6                                                                                               | Meter accessible                | Yes                  | Meter room ventilated                | Yes                                                                                 | Working pressure at meter               | 20.87                                                                                                                                                                                                                             | 18.42                                 |  |
| ECV labelled                                                                                                                                            | Yes                                                                                              | Does ECV operate easily         | Yes                  | Adequate gas isolation               | Yes                                                                                 | Suitably sleeved Area Adjacent Meter    | Yes                                                                                                                                                                                                                               | Meter Labelling Correct               |  |
| Pipework colour coded /identified from point of Test                                                                                                    | Yes                                                                                              | Line diagram at meter (current) | Yes                  | Clear of combustibles                | N/A                                                                                 | Installation cross bonded               | Yes                                                                                                                                                                                                                               | Yes                                   |  |
| Gas pipe supported (Where Visible) from point of Test                                                                                                   | Yes                                                                                              | Meter Location                  | Outside meter box    |                                      | Flue Dilution (CO₂) %                                                               | N/A                                     | Air Sample (CO₂) %                                                                                                                                                                                                                | N/A                                   |  |
| Manometer Make                                                                                                                                          | Testo                                                                                            | Serial No                       | 26884240             | Analyser Make                        | Testo                                                                               | Serial No                               | 61857248                                                                                                                                                                                                                          |                                       |  |
| Description of work: Boiler service and co device check                                                                                                 |                                                                                                  |                                 |                      |                                      |                                                                                     |                                         |                                                                                                                                                                                                                                   |                                       |  |
| Defects                                                                                                                                                 |                                                                                                  |                                 |                      |                                      | Remedial work required                                                              |                                         |                                                                                                                                                                                                                                   |                                       |  |
| No 1                                                                                                                                                    | Boiler had no power due to a wires screwed to right in the terminals which caused exposed wiring |                                 |                      |                                      | I have repaired wiring fault and now boiler working                                 |                                         |                                                                                                                                                                                                                                   |                                       |  |
| No 2                                                                                                                                                    | Co alarm lost                                                                                    |                                 |                      |                                      | New co alarm installed                                                              |                                         |                                                                                                                                                                                                                                   |                                       |  |
| No 3                                                                                                                                                    |                                                                                                  |                                 |                      |                                      |                                                                                     |                                         |                                                                                                                                                                                                                                   |                                       |  |
| No 4                                                                                                                                                    |                                                                                                  |                                 |                      |                                      |                                                                                     |                                         |                                                                                                                                                                                                                                   |                                       |  |
| No 5                                                                                                                                                    |                                                                                                  |                                 |                      |                                      |                                                                                     |                                         |                                                                                                                                                                                                                                   |                                       |  |
| No 6                                                                                                                                                    |                                                                                                  |                                 |                      |                                      |                                                                                     |                                         |                                                                                                                                                                                                                                   |                                       |  |
| No 7                                                                                                                                                    |                                                                                                  |                                 |                      |                                      |                                                                                     |                                         |                                                                                                                                                                                                                                   |                                       |  |
| No 8                                                                                                                                                    |                                                                                                  |                                 |                      |                                      |                                                                                     |                                         |                                                                                                                                                                                                                                   |                                       |  |
| Parts used                                                                                                                                              |                                                                                                  |                                 | Part Number          |                                      | Qty                                                                                 |                                         | Declaration of Gas safety: I confirm that all of the work described on this form has been satisfactorily completed in accordance with the current Gas Safety (Installation & Use) regulations, industry standards and procedures. |                                       |  |
|                                                                                                                                                         |                                                                                                  |                                 |                      |                                      |                                                                                     |                                         |                                                                                                                                                                                                                                   |                                       |  |
|                                                                                                                                                         |                                                                                                  |                                 |                      |                                      |                                                                                     |                                         |                                                                                                                                                                                                                                   |                                       |  |
|                                                                                                                                                         |                                                                                                  |                                 |                      |                                      |                                                                                     |                                         |                                                                                                                                                                                                                                   |                                       |  |
| Print Name                                                                                                                                              | Jack Williams                                                                                    |                                 | Engineer's Signature |                                      |  |                                         |                                                                                                                                                                                                                                   |                                       |  |
| The work has been carried out to my satisfaction. I agree to pay for all chargeable work carried out and the cost of any parts ordered and/or supplied. |                                                                                                  |                                 |                      |                                      |                                                                                     |                                         |                                                                                                                                                                                                                                   |                                       |  |
| Print Name                                                                                                                                              | No person present                                                                                |                                 | Customer Signature   |                                      |                                                                                     |                                         |                                                                                                                                                                                                                                   |                                       |  |

## Tightness Test Carried out from this Valve 'Label'

### Measurement protocol

#### General information

|                    |                                    |                       |
|--------------------|------------------------------------|-----------------------|
| <b>Customer</b>    | <b>Name of measurement program</b> | <b>Tightness test</b> |
| 5 Cryfield cottage | Date of measurement                | 01/07/2026 10:38:01   |

#### Instrument information

|                                      |                               |
|--------------------------------------|-------------------------------|
| <b>Instrument name/Serial number</b> | <b>Measurement parameters</b> |
| testo 510 (46527985)                 | Differential pressure         |

#### Measurement parameters

|                               |                      |                          |                     |
|-------------------------------|----------------------|--------------------------|---------------------|
| Measuring mode                | Timed                | Maximum pressure drop    | 1.00 mbar           |
| Measuring cycle               | 20 sec               | Pressure start (P Start) | 20.90 mbar          |
| Use stabilisation time        | Yes                  | Measurement result       | Passed              |
| Measurement duration (target) | 2 min 0 sec          | Start time               | 01/07/2026 10:32:43 |
| Pressure probe                | testo 510 (46527985) | End                      | 01/07/2026 10:34:43 |
| Fuel type                     | Natural gas          | Duration                 | 2 min 0 sec         |

#### Measurement

|                       |            |
|-----------------------|------------|
| Maximum pressure drop | 1.00 mbar  |
| Final pressure drop   | -0.05 mbar |

| Date/Time           | ΔP current [mbar] | 985 [mbar] |
|---------------------|-------------------|------------|
| 01/07/2026 10:32:43 |                   | 20.90      |
| 01/07/2026 10:33:03 | 0.00              | 20.90      |
| 01/07/2026 10:33:23 | -0.01             | 20.89      |
| 01/07/2026 10:33:43 | -0.02             | 20.88      |
| 01/07/2026 10:34:03 | -0.03             | 20.87      |
| 01/07/2026 10:34:23 | -0.04             | 20.86      |
| 01/07/2026 10:34:43 | -0.05             | 20.85      |



## Appliance Flue Termination




## Warning Label 'if Applicable'

## CO Expiry Date

## Location of CO Alarm

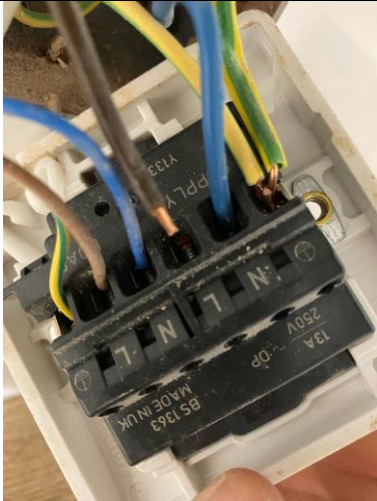

| Photo of Unsafe Situation | Defect 1                                                                          | Defect 2                                                                            |
|---------------------------|-----------------------------------------------------------------------------------|-------------------------------------------------------------------------------------|
|                           |  |  |
| Defect 3                  | Defect 4                                                                          | Defect 5                                                                            |
|                           |                                                                                   |                                                                                     |
| Defect 6                  | Defect 7                                                                          | Defect 8                                                                            |
|                           |                                                                                   |                                                                                     |
