


Gas Tightness Test									
Gas tightness test carried out (Yes / No)	Yes	Total Installation volume (m³)	0.0032	Max allowable pressure drop (mbar)	4	Type of gauge used (water / electronic)	Electric	Tightness test result (Pass / Fail)	
Where was the Test carried out from?	ECV	Let by test duration (mins)	1	Volume smallest occupied space (m³)	N/A	Smell of gas	N/A	Pass	
Scope of work (e.g. IGE/UP/1 or 1A or 1B)	IGE/UP/1B	Stabilisation period (mins)	1	Tightness test pressure (TTP) (mbar)	21.87	CO Alarm			
						CO Alarm Installed	Date Of Expiry	CO Pass/Fail	
Installation (New / Existing / Extension)	Existing	Tightness test duration (mins)	2	Actual pressure drop (mbar)	0	Yes	06/2033	Pass	
Meter Information									
Gas Meter Present	Yes	Meter room secure	Yes	Meter room key labelled	N/A	Standing pressure (mbar)		Working pressure at Appliances (mbar)	
Meter size	U6	Meter accessible	Yes	Meter room ventilated	N/A	Working pressure at meter	20.87	17.49	
ECV labelled	Yes	Does ECV operate easily	Yes	Adequate gas isolation	Yes	Suitably sleeved Area Adjacent Meter	Yes	Meter Labelling Correct	
Pipework colour coded /identified from point of Test	N/A	Line diagram at meter (current)	N/A	Clear of combustibles	N/A	Installation cross bonded	Yes	Yes	
Gas pipe supported (Where Visible) from point of Test	Yes	Meter Location	Outside meter box		Flue Dilution (CO ₂) %	N/A	Air Sample (CO ₂) %	N/A	
Manometer Make	Testo	Serial No	26884240	Analyser Make	Testo	Serial No	61857248		
Description of work: Boiler service hob service and co device check									
Defects					Remedial work required				
No 1									
No 2									
No 3									
No 4									
No 5									
No 6									
No 7									
No 8									
Parts used			Part Number		Qty		Declaration of Gas safety: I confirm that all of the work described on this form has been satisfactorily completed in accordance with the current Gas Safety (Installation & Use) regulations, industry standards and procedures.		
			New co alarm		1				
Print Name	Jack Williams		Engineer's Signature						
The work has been carried out to my satisfaction. I agree to pay for all chargeable work carried out and the cost of any parts ordered and/or supplied.									
Print Name	No person present		Customer Signature						

Tightness Test Carried out from this Valve 'Label'



Measurement protocol

General information

Customer	Name of measurement program	Tightness test
7 Crayfield Cottage	Date of measurement	01/04/2026 11:24:46

Instrument information

Instrument name/Serial number	Measurement parameters
teso 510 (46884240)	Differential pressure

Measurement parameters

Measuring mode	Timed	Maximum pressure drop	4.00 mbar
Measuring cycle	20 sec	Pressure start (P_start)	21.57 mbar
Use stabilisation time	Yes	Measurement result	Passed
Measurement duration (range)	2 min 0 sec	Start time	01/04/2026 11:22:29
Pressure probe (range)	teso 510 (46884240)	End	01/04/2026 11:24:29
Fuel type	Natural gas	Duration	2 min 0 sec




Measurement

Maximum pressure drop	4.00 mbar
Final pressure drop	0.81 mbar

Date/Time	ΔP [mbar]	ΔP current [mbar]
01/04/2026 11:22:29	21.87	-
01/04/2026 11:23:49	20.02	0.15
01/04/2026 11:23:09	22.17	0.30
01/04/2026 11:23:29	22.31	0.44
01/04/2026 11:23:49	22.45	0.58
01/04/2026 11:24:09	22.57	0.70
01/04/2026 11:24:29	22.68	0.81



Appliance Flue Termination



Warning Label 'if Applicable'

CO Expiry Date

Location of CO Alarm

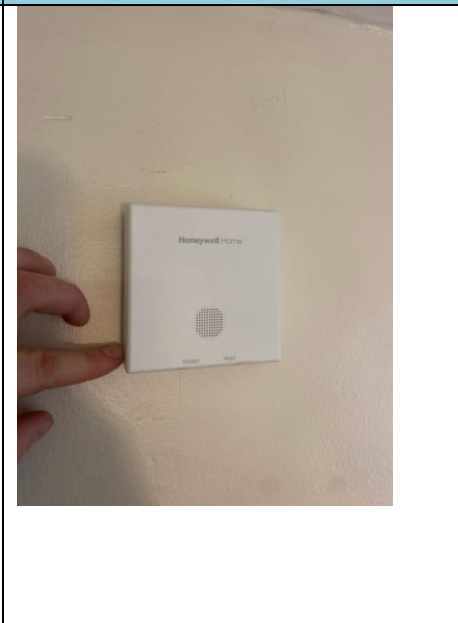
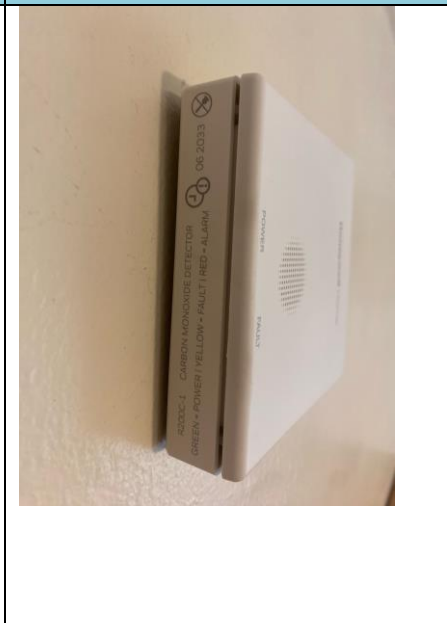



Photo of Unsafe Situation	Defect 1	Defect 2
Defect 3	Defect 4	Defect 5
Defect 6	Defect 7	Defect 8
