




Gas Tightness Test									
Gas tightness test carried out (Yes / No)	Yes	Total Installation volume (m³)		Max allowable pressure drop (mbar)	4.1	Type of gauge used (water / electronic)	Electric	Tightness test result (Pass / Fail)	
Where was the Test carried out from?	ECV	Let by test duration (mins)	1	Volume smallest occupied space (m³)		Smell of gas	N/A	Pass	
Scope of work (e.g. IGE/UP/1 or 1A or 1B)	IGE/UP/1B	Stabilisation period (mins)	1	Tightness test pressure (TTP) (mbar)	19.96	CO Alarm			
						CO Alarm Installed	Date Of Expiry	CO Pass/Fail	
Installation (New / Existing / Extension)	Existing	Tightness test duration (mins)	2	Actual pressure drop (mbar)	0	Yes	07/2033	Pass	
Meter Information									
Gas Meter Present	Yes	Meter room secure	N/A	Meter room key labelled	N/A	Standing pressure (mbar)	25.67	Working pressure at Appliances (mbar)	
Meter size	U6	Meter accessible	Yes	Meter room ventilated	N/A	Working pressure at meter	20.78	19.12	
ECV labelled	Yes	Does ECV operate easily	Yes	Adequate gas isolation	Yes	Suitably sleeved Area Adjacent Meter	Yes	Meter Labelling Correct	
Pipework colour coded /identified from point of Test	Yes	Line diagram at meter (current)	N/A	Clear of combustibles	N/A	Installation cross bonded	Yes	Yes	
Gas pipe supported (Where Visible) from point of Test	Yes	Meter Location	Outside meter box		Flue Dilution (CO <sub>2</sub> ) %	N/A	Air Sample (CO <sub>2</sub> ) %	N/A	
Manometer Make	Testo	Serial No	26884240	Analyser Make	Testo	Serial No	61857248		
Description of work: Boiler service and co device check									
Defects					Remedial work required				
No 1									
No 2									
No 3									
No 4									
No 5									
No 6									
No 7									
No 8									
Parts used			Part Number		Qty		Declaration of Gas safety: I confirm that all of the work described on this form has been satisfactorily completed in accordance with the current Gas Safety (Installation & Use) regulations, industry standards and procedures.		
Print Name	Jack Williams		Engineer's Signature						
The work has been carried out to my satisfaction. I agree to pay for all chargeable work carried out and the cost of any parts ordered and/or supplied.									
Print Name	No person present		Customer Signature						

## Tightness Test Carried out from this Valve 'Label'



### Measurement protocol

Customer information		Name of measurement program	
Customer	1. Valuable staff Ltd	Program	Tightness test
Date of measurement	07/05/2025 10:53:43		
Measurement information		Measurement parameters	
Measurement name/Serial number	testo 510 (46884240)	Measurement parameters	Differential pressure
Measurement parameters			
Measuring mode	Timed	Maximum pressure drop	4.10 mbar
Measuring cycle	20 sec	Pressure start (P_start)	10.98 mbar
Use stabilisation time	Yes	Measurement result	Passed
Measurement duration	2 min 0 sec	Start time	07/05/2025 10:51:38
Target		End	07/05/2025 10:53:38
Pressure probe	testo 510 (46884240)	Duration	2 min 0 sec
Fuel type	Natural gas		
Measurement results			
Maximum pressure drop		4.10 mbar	
Final pressure drop		0.07 mbar	
Date/Time	ΔP0 (mbar)	ΔP current (mbar)	
07/05/2025 10:51:38	10.98		
07/05/2025 10:51:54	20.01	0.06	
07/05/2025 10:52:14	20.01	0.06	
07/05/2025 10:52:35	20.02	0.06	
07/05/2025 10:52:55	20.02	0.06	
07/05/2025 10:53:15	20.03	0.07	
07/05/2025 10:53:35	20.03	0.07	

## Appliance Flue Termination



Warning Label 'if Applicable'

CO Expiry Date

Location of CO Alarm

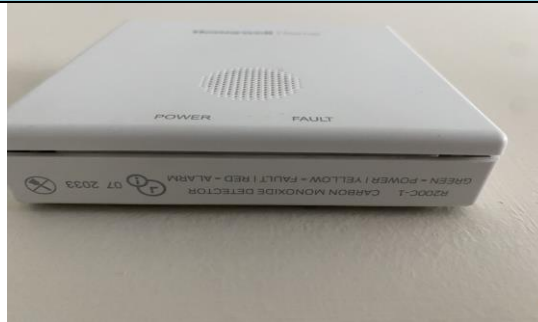


Photo of Unsafe Situation	Defect 1	Defect 2
Defect 3	Defect 4	Defect 5
Defect 6	Defect 7	Defect 8
