
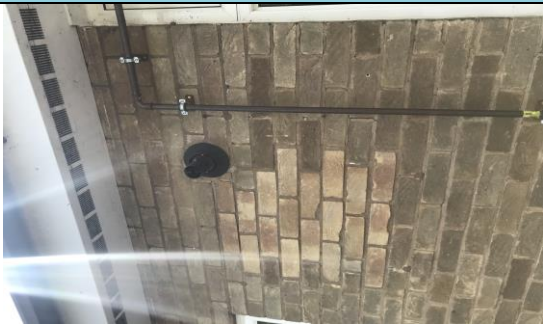


Gas Tightness Test									
Gas tightness test carried out (Yes / No)	Yes	Total Installation volume (m³)	0.2	Max allowable pressure drop (mbar)	0.7	Type of gauge used (water / electronic)	Electric	Tightness test result (Pass / Fail)	
Where was the Test carried out from?	ECV	Let by test duration (mins)	1	Volume smallest occupied space (m³)	3.24	Smell of gas	N/A	Pass	
Scope of work (e.g. IGE/UP/1 or 1A or 1B)	IGE/UP/1B	Stabilisation period (mins)	1	Tightness test pressure (TTP) (mbar)	20	CO Alarm			
						CO Alarm Installed	Date Of Expiry	CO Pass/Fail	
Installation (New / Existing / Extension)	Existing	Tightness test duration (mins)	2	Actual pressure drop (mbar)	0	Yes	09/2024	Pass	
Meter Information									
Meter Location	Plant room	Meter room secure	Yes	Meter room key labelled	Card access	Standing pressure at meter (mbar)	26	Working pressure at Appliances (mbar)	
Meter size	QA 65 turbine meter	Meter accessible	Yes	Meter room ventilated	Yes	Working pressure at meter	25	22	
ECV labelled	Yes	Does ECV operate easily	Yes	Adequate gas isolation	Yes	Suitably sleeved Area Adjacent Meter	Yes	Meter Labelling Correct	
Pipework colour coded /identified from point of Test	Yes	Line diagram at meter (current)	No	Clear of combustibles	Yes	Installation cross bonded	Yes	No labels	
Gas pipe supported (Where Visible) from point of Test	Yes				Flue Dilution (CO ₂) %	N/a	Air Sample (CO ₂) %	N/a	
Manometer Make	Testo	Serial No	N/a	Analyser Make	61857248	Serial No	Testo		
Description of work: Tightness test, boiler and hob serviced and co alarm tested also changed r/h green boiler case clip and aav in boiler									
Defects					Remedial work required				
No 1	Butterfly valve on hob has tendency to leak				Recommend removing butterfly valve and replacing with lever valve				
No 2	R/h green boiler case clip broken				Replaced on service				
No 3	Aav leaking in boiler				Replaced leaking aav with new on service				
No 4									
No 5									
No 6									
No 7									
No 8									
Parts used			Part Number		Qty		Declaration of Gas safety: I confirm that all of the work described on this form has been satisfactorily completed in accordance with the current Gas Safety (Installation & Use) regulations, industry standards and procedures.		
			8-718-686-621-0		1				
R/h green boiler case clip					1				
Automatic air vent									
Print Name	Sean Moloney		Engineer's Signature						
The work has been carried out to my satisfaction. I agree to pay for all chargeable work carried out and the cost of any parts ordered and/or supplied.									
Print Name	No person present		Customer Signature						

Tightness Test Carried out from this Valve 'Label'



Appliance Flue Termination



Warning Label 'if Applicable'

CO Expiry Date




Location of CO Alarm



Photo of Unsafe Situation

Defect 1


Defect 2

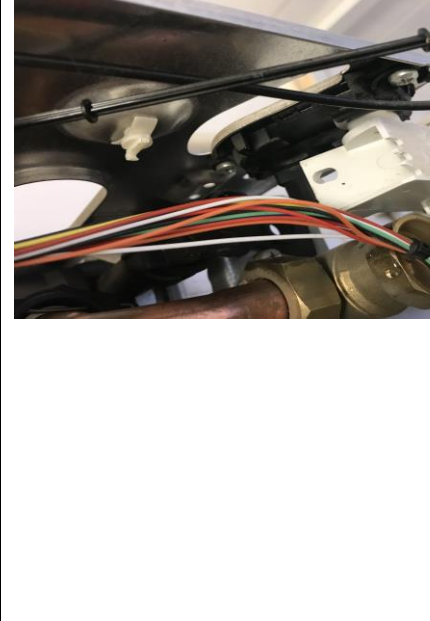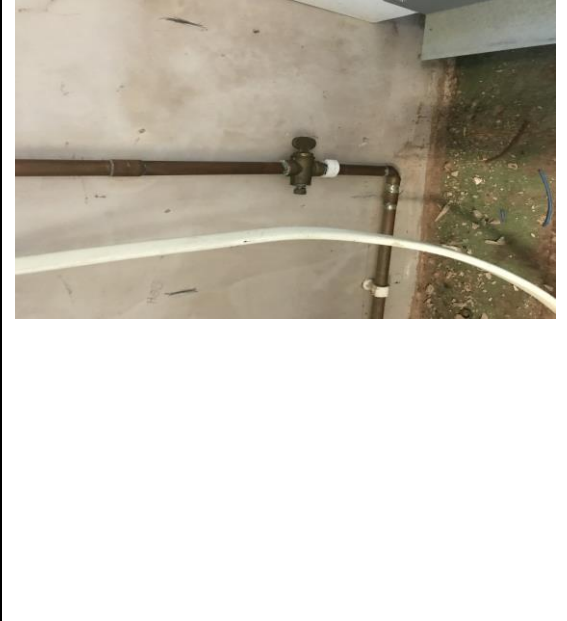

Defect 3

Defect 4

Defect 5



Defect 6

Defect 7

Defect 8

